

Beaufort County Public Works Stormwater Infrastructure

Project Summary

Project Summary: Alljoy Area - Fairfax Street

Activity: Routine/Preventive Maintenance

Duration: 03/10/2021 - 07/12/2021

Narrative Description of Project:

Project improved 733 L.F. of drainage system. Cleaned out 661 L.F. of roadside ditch. Installed 72 L.F. of roadside pipe and hydroseeded for erosion control.

2021-534 / Alljoy Area	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
AUDIT / Audit Project	2.50	\$81.85	\$0.00	\$0.00	\$0.00	\$50.53	\$132.38
DEBREM / Debris Removal - Jobsite	88.00	\$1,873.28	\$371.28	\$140.40	\$0.00	\$1,157.52	\$3,542.48
DPINS / Driveway Pipe - Installed	40.00	\$874.56	\$258.37	\$922.54	\$0.00	\$511.20	\$2,566.67
HAUL / Hauling	143.00	\$3,921.33	\$2,725.58	\$3,547.30	\$0.00	\$2,924.26	\$13,118.47
HYDR / Hydroseeding	16.00	\$350.12	\$55.21	\$66.75	\$0.00	\$188.40	\$660.48
RPWO / Repaired Washout	40.00	\$842.48	\$123.56	\$91.20	\$0.00	\$390.20	\$1,447.44
RSDCL / Roadside Ditch - Cleanout	104.00	\$2,206.40	\$312.11	\$160.80	\$0.00	\$1,514.00	\$4,193.31
UC / Utility Coordination	1.00	\$24.70	\$0.00	\$0.00	\$0.00	\$13.23	\$37.93
UTLOC / Utility locates	4.00	\$98.80	\$0.00	\$0.00	\$0.00	\$52.92	\$151.72
WSDR / Workshelf - Dressed	40.00	\$874.56	\$128.49	\$147.88	\$0.00	\$511.20	\$1,662.13
Grand Total	478.50	\$11,148.08	\$3,974.60	\$5,076.87	\$0.00	\$7,313.45	\$27,513.01

(Before)




(During)



(After)



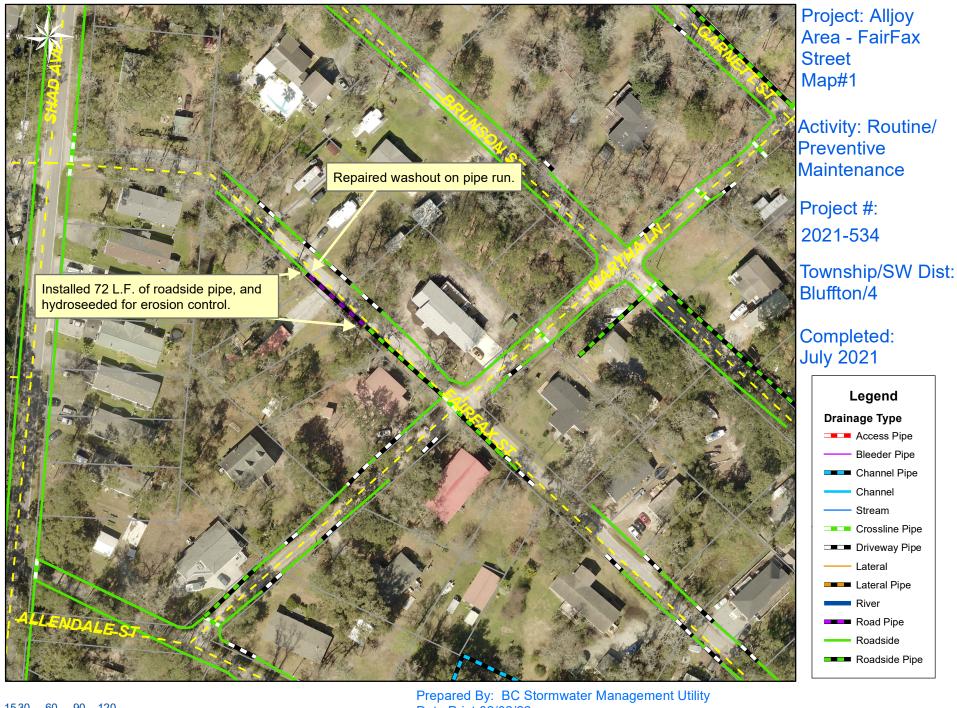

0 1530

1 inch = 100 feet

Date Print:02/02/22

File:C:\project summaries map/FairFax Rd Map#1 2021-534



0 20 40 80 120 160

Date Print:02/02/22

File:C:\project summaries map/Alljoy Rd. and Fairfax Rd.Map#2_2022-534
