



Beaufort County Public Works
Stormwater Infrastructure
Project Summary

Project Summary: Palmetto Beach Lane

Activity: Routine/Preventive Maintenance

Duration: 10/07/2021 - 01/26/2022

Narrative Description of Project:

Project improved 727 L.F. of drainage system. Cleaned out 727 L.F. of roadside ditch and installed (1) driveway pipe.

2022-515 / Palmetto Beach Lane

	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
ASBUILT / Asbuilt - Project	8.00	\$199.80	\$17.40	\$18.41	\$0.00	\$123.32	\$358.93
AUDIT / Audit Project	0.50	\$15.59	\$0.00	\$0.00	\$0.00	\$9.62	\$25.21
DPINS / Driveway Pipe - Installed	24.00	\$574.41	\$174.38	\$304.74	\$0.00	\$246.64	\$1,300.17
HAUL / Hauling	32.00	\$877.69	\$533.68	\$819.65	\$0.00	\$491.88	\$2,722.91
RSDCL / Roadside Ditch - Cleanout	48.00	\$1,148.77	\$221.65	\$52.38	\$0.00	\$493.28	\$1,916.08
SITEINSP / Site Inspection	3.00	\$93.51	\$13.05	\$50.10	\$0.00	\$57.72	\$214.38
UTLOC / Utility locates	0.50	\$12.35	\$0.00	\$0.00	\$0.00	\$6.62	\$18.97
Grand Total	116.00	\$2,922.12	\$960.16	\$1,245.29	\$0.00	\$1,429.08	\$6,556.64

Before




During



After



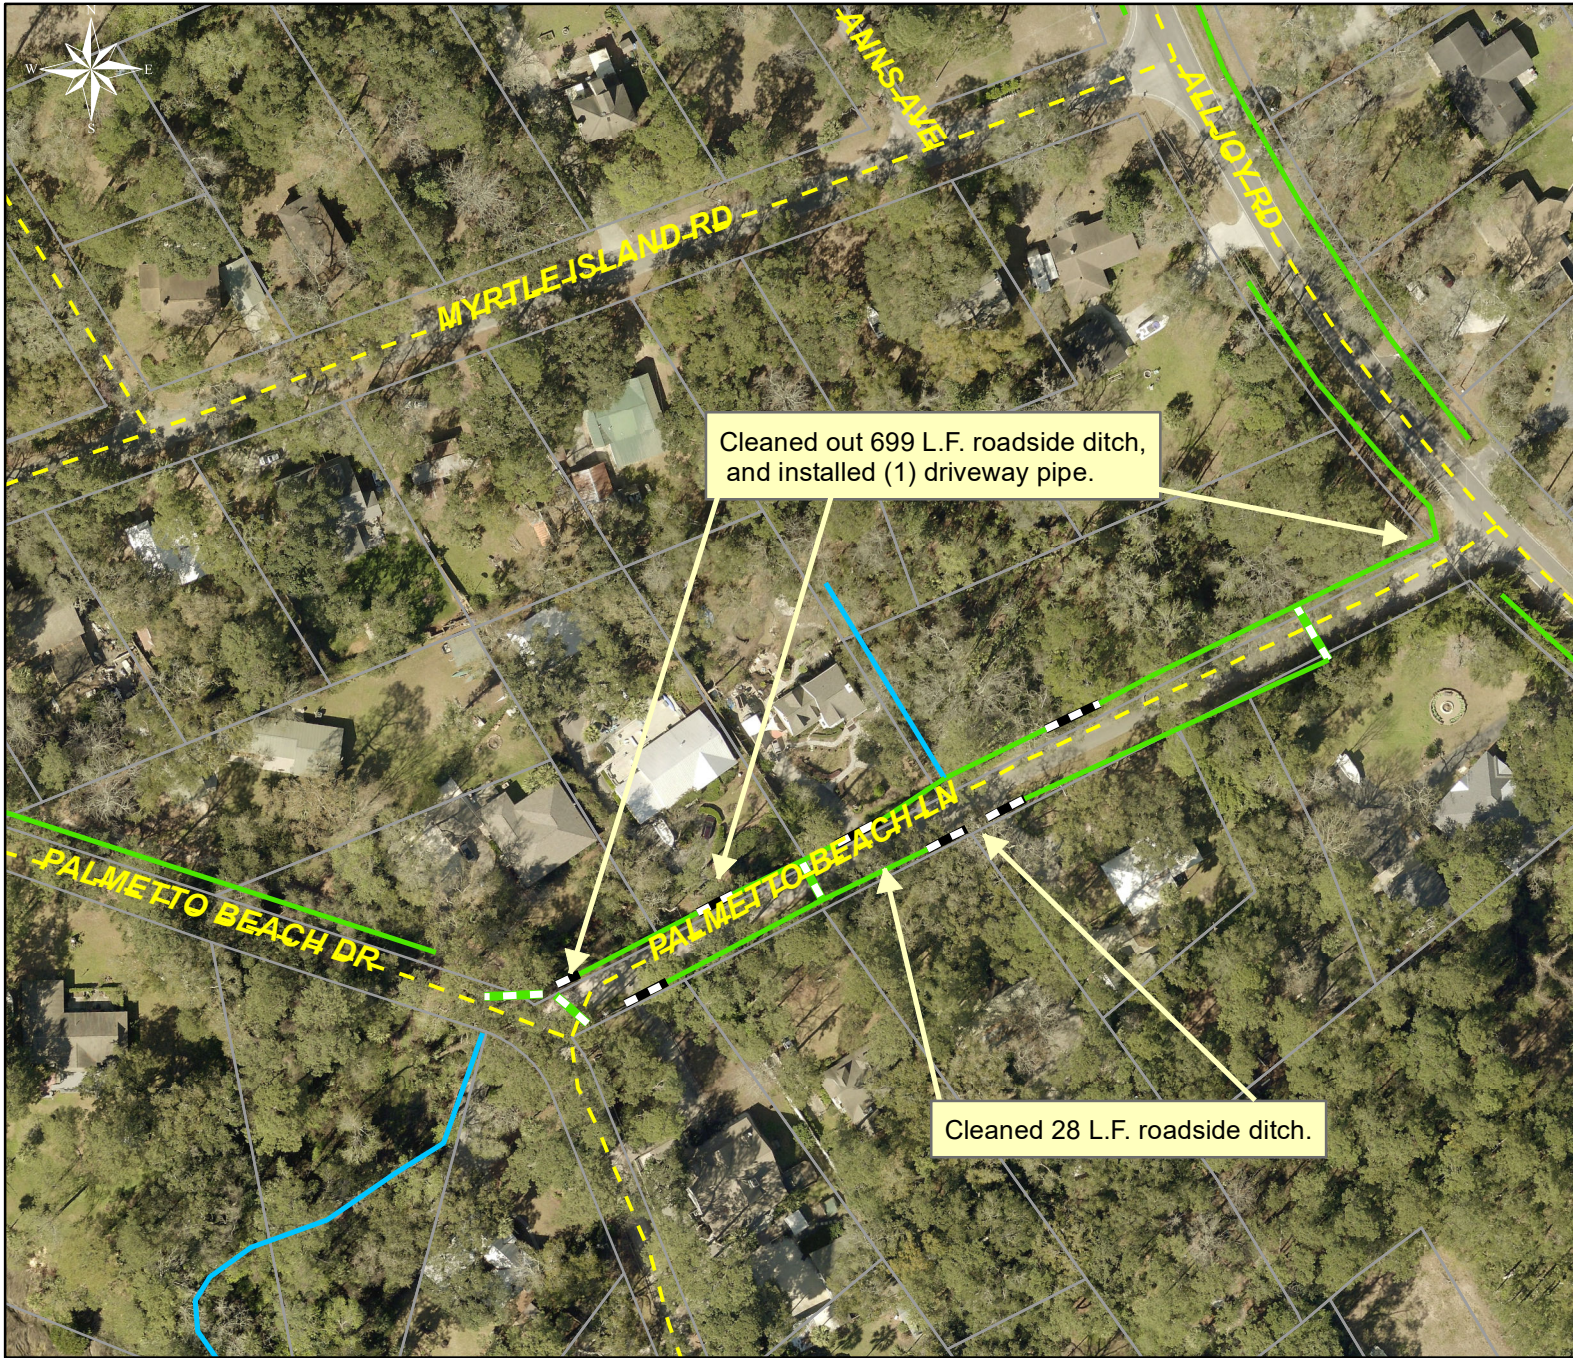

Project: Palmetto Beach Ln

Activity: Routine/ Preventive Maintenance














Project #: 2022-515

Township/SW Dist: Bluffton/4

Completed: January 2022

Legend

Drainage Type

-  Access Pipe
-  Bleeder Pipe
-  Channel Pipe
-  Channel
-  Stream
-  Crossline Pipe
-  Driveway Pipe
-  Lateral
-  Lateral Pipe
-  River
-  Road Pipe
-  Roadside
-  Roadside Pipe

0 20 40 80 120 160 Feet

1 inch = 130 feet

Prepared By: BC Stormwater Management Utility
 Date Print: 05/13/22
 File: C:\project summaries map\Palmetto Beach Ln_2022-515
