

## Beaufort County Public Works Stormwater Infrastructure Project Summary

Project Summary: ToHHI - Arrow Road (Reimbursement)

Activity: Routine/Preventive Maintenance

## Narrative Description of Project:

Duration: 4/18/16 - 6/16/16

Project improved 2,826 L.F. of drainage system. Cleaned out (2) catch basins and 2,742 L.F. of roadside ditch. Jetted (1) crossline pipe, (19) driveway pipes and 84 L.F. of channel pipe. Hydroseeded for erosion control.

2016-590 / ToHHI - Arrow Road	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
	Hours	COST	COST	COST	Cost	Labor	Total Cost
AUDIT / Audit Project	2.0	\$46.98	\$0.00	\$0.00	\$0.00	\$26.46	\$73.44
CBCO / Catch basin - clean out	20.0	\$469.80	\$86.80	\$57.90	\$0.00	\$308.90	\$923.40
DLO / Ditch Layout	98.0	\$2,170.82	\$177.28	\$65.08	\$0.00	\$1,198.30	\$3,611.47
DPJT / Driveway Pipe - Jetted	45.0	\$1,063.10	\$363.20	\$162.20	\$0.00	\$700.15	\$2,288.65
HAUL / Hauling	184.0	\$4,084.24	\$1,470.12	\$641.03	\$0.00	\$2,644.44	\$8,839.83
HYDR / Hydroseeding	55.0	\$1,224.09	\$181.11	\$1,041.27	\$0.00	\$732.50	\$3,178.96
LM / Loading Materials	35.0	\$821.98	\$265.97	\$57.65	\$0.00	\$475.80	\$1,621.40
ONJV / Onsite Job Visit	26.0	\$825.14	\$92.28	\$48.87	\$0.00	\$582.58	\$1,548.87
PROFS / Professional Services	0.0	\$0.00	\$0.00	\$0.00	\$717.15	\$0.00	\$717.15
RMTRD / Remove trees - Ditch	48.0	\$1,066.63	\$202.70	\$39.39	\$0.00	\$533.00	\$1,841.72
RSDCL / Roadside Ditch - Cleanout	576.0	\$12,750.12	\$1,955.12	\$385.22	\$0.00	\$7,660.83	\$22,751.29
RSPJ / Roadside Pipe - Jetted	40.0	\$890.99	\$58.23	\$41.53	\$0.00	\$530.90	\$1,521.65
TC / Traffic Control - Jobsite	90.0	\$1,997.78	\$264.05	\$68.99	\$0.00	\$1,198.30	\$3,529.12
UTLOC / Utility locates	1.5	\$37.05	\$0.00	\$0.00	\$0.00	\$19.85	\$56.90
2016-590 / ToHHI - Arrow Road Sub Total	1,220.5	\$27,448.71	\$5,116.86	\$2,609.12	\$717.15	\$16,612.00	\$52,503.84

Grand Total	1,220.5	\$27,448.71	\$5,116.86	\$2,609.12	\$717.15	\$16,612.00	\$52,503.84












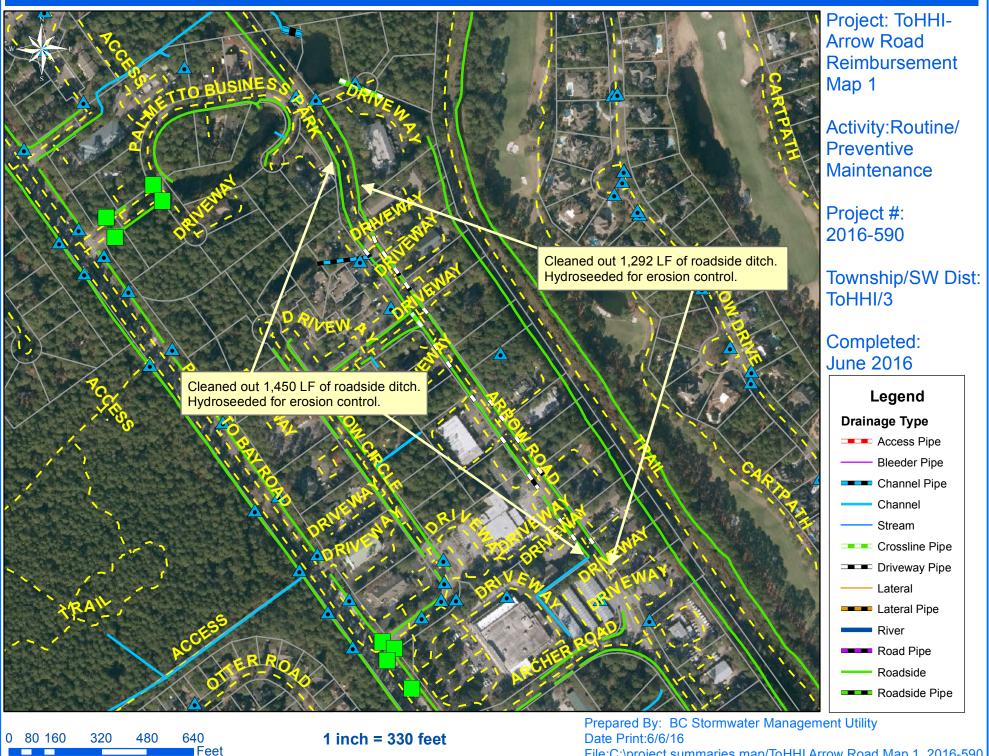

File:C:\project summaries map/ToHHI Arrow Road Map 1\_2016-590

