



**Beaufort County Public Works**  
**Stormwater Infrastructure**  
*Project Summary*

**Project Summary:** Scott Hill Road Channel #2

**Activity:** Routine/Preventive Maintenance

**Duration:** 06/06/2023 - 06/12/2023

**Narrative Description of Project:**

Project improved 2,867 L.F. of drainage system. Cleaned out 1,979 L.F. of channel and 888 L.F. of roadside ditch.

<b>2023-609 / Scott Hill Road Channel #2</b>	<b>Labor Hours</b>	<b>Labor Cost</b>	<b>Equipment Cost</b>	<b>Material Cost</b>	<b>Contractor Cost</b>	<b>Indirect Cost</b>	<b>Total Cost</b>
AUDIT / Audit Project	1.50	\$50.60	\$0.00	\$0.00	\$0.00	\$31.23	\$81.83
CCO / Channel - cleaned out	80.00	\$2,329.04	\$234.16	\$112.55	\$0.00	\$1,437.68	\$4,113.43
HAUL / Hauling	40.00	\$1,235.20	\$762.40	\$166.46	\$0.00	\$304.96	\$2,469.02
ONJV / Onsite Job Visit	12.00	\$603.60	\$52.20	\$16.68	\$0.00	\$372.60	\$1,045.08
RSDCL / Roadside Ditch - Cleanout	32.00	\$862.10	\$118.26	\$90.04	\$0.00	\$532.16	\$1,602.56
<b>Grand Total</b>	<b>165.50</b>	<b>\$5,080.54</b>	<b>\$1,167.02</b>	<b>\$385.73</b>	<b>\$0.00</b>	<b>\$2,678.63</b>	<b>\$9,311.92</b>

**(No Pictures Available)**


Project: Scott Hill Road Channel #2

Activity: Routine/ Preventive Maintenance

Project #: 2023-609

Township/SW Dist: St. Helena Island/8

Completed: June 2023

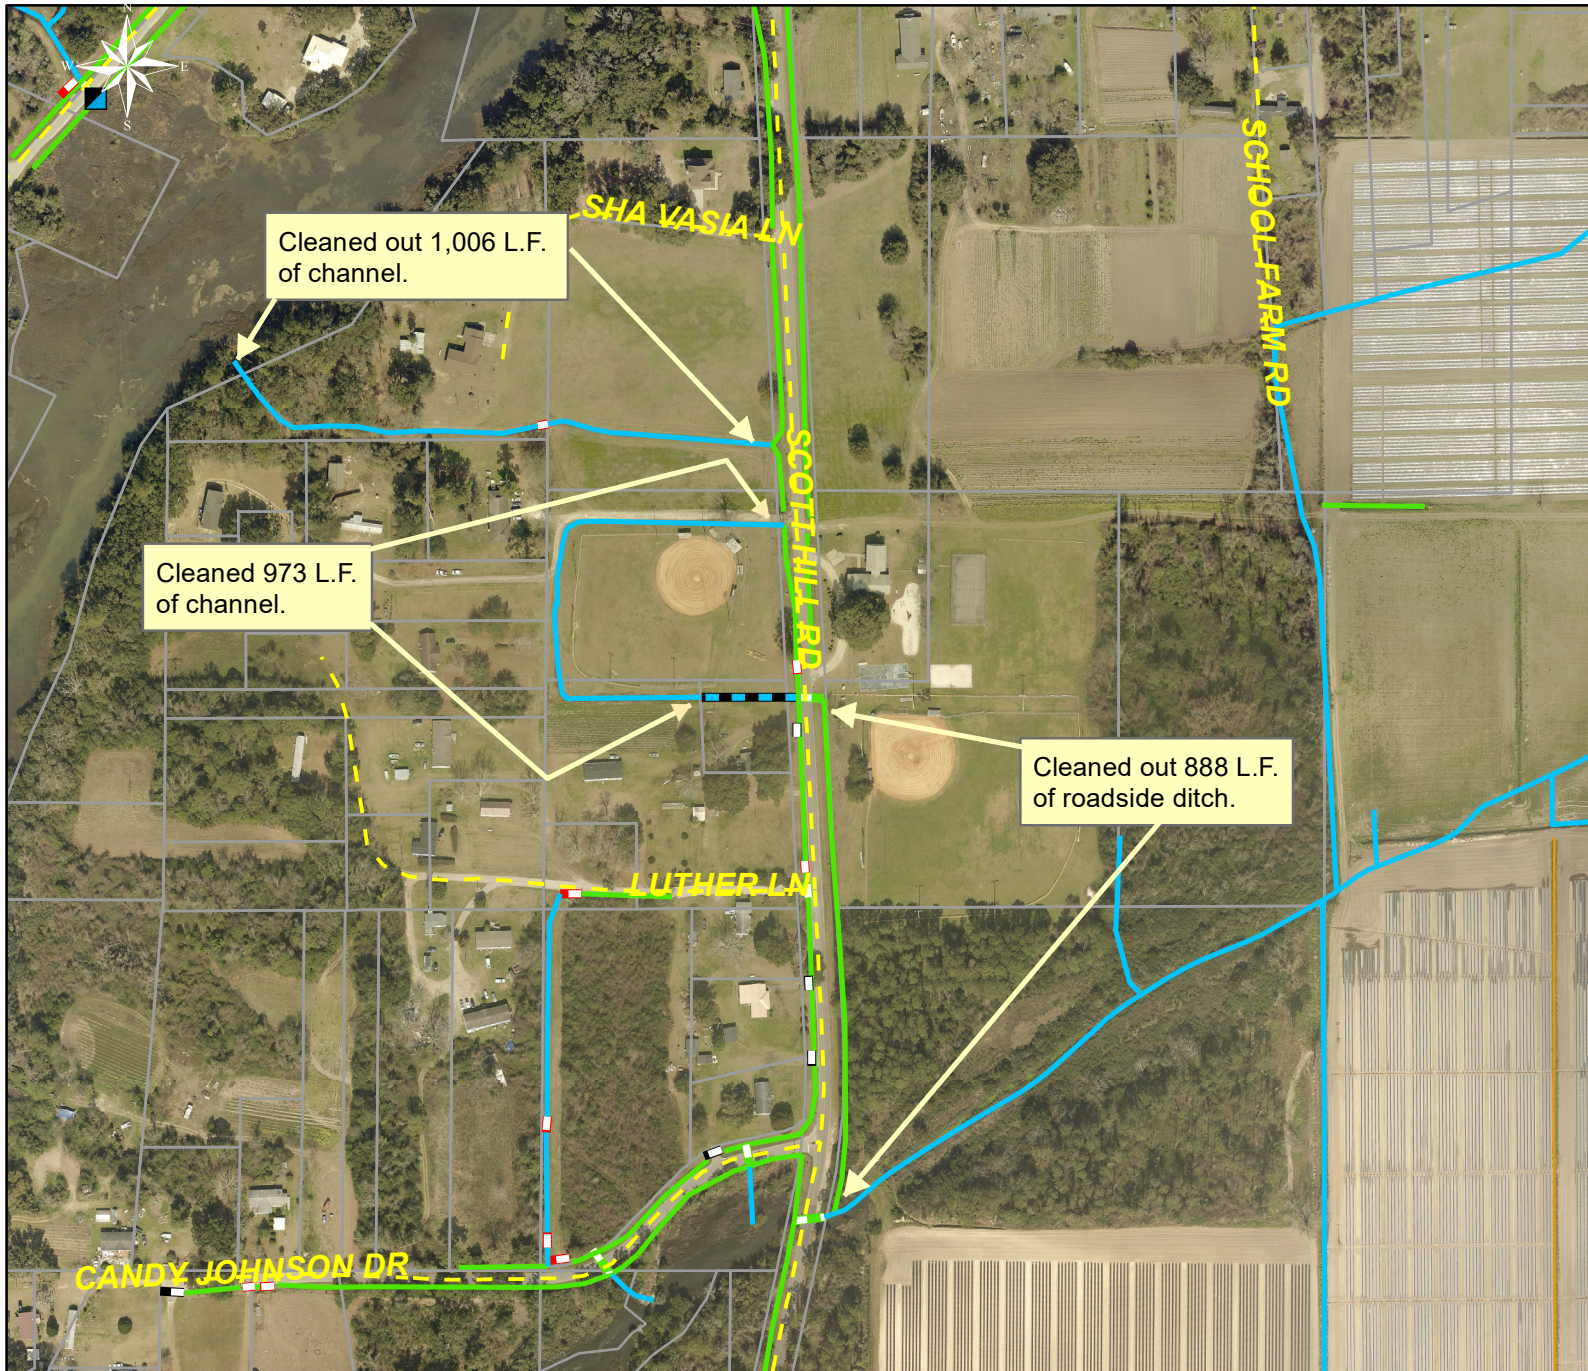

Legend	
Drainage Type	
	Access Pipe
	Bleeder Pipe
	Channel Pipe
	Channel
	Stream
	Crossline Pipe
	Driveway Pipe
	Lateral
	Lateral Pipe
	River
	Road Pipe
	Roadside
	Roadside Pipe



1 inch = 330 feet
