



**Beaufort County Public Works**  
**Stormwater Infrastructure**  
Project Summary

**Project Summary:** Kato Lane Channel

**Activity:** Routine/Preventive Maintenance

**Duration:** 11/21/2022 -12/05/2022

**Narrative Description of Project:**

Project improved 2,827 L.F. of drainage system. Cleaned out 2,127 L.F. of channel ditch and reconstructed 700 L.F. of channel.

**2023-539 / Kato Lane Channel**

	<b>Labor Hours</b>	<b>Labor Cost</b>	<b>Equipment Cost</b>	<b>Material Cost</b>	<b>Contractor Cost</b>	<b>Indirect Cost</b>	<b>Total Cost</b>
AUDIT / Audit Project	1.50	\$49.11	\$0.00	\$0.00	\$0.00	\$30.32	\$79.43
CCO / Channel - cleaned out	72.00	\$2,274.09	\$499.73	\$534.66	\$0.00	\$1,403.76	\$4,712.24
CREC / Channel - reconstructed	72.00	\$2,274.09	\$561.66	\$342.27	\$0.00	\$1,403.76	\$4,581.78
HAUL / Hauling	32.00	\$1,073.64	\$609.92	\$264.68	\$0.00	\$662.72	\$2,610.96
<b>Grand Total</b>	<b>177.50</b>	<b>\$5,670.94</b>	<b>\$1,671.31</b>	<b>\$1,141.61</b>	<b>\$0.00</b>	<b>\$3,500.56</b>	<b>\$11,984.41</b>

**Before**




**During**



**After**





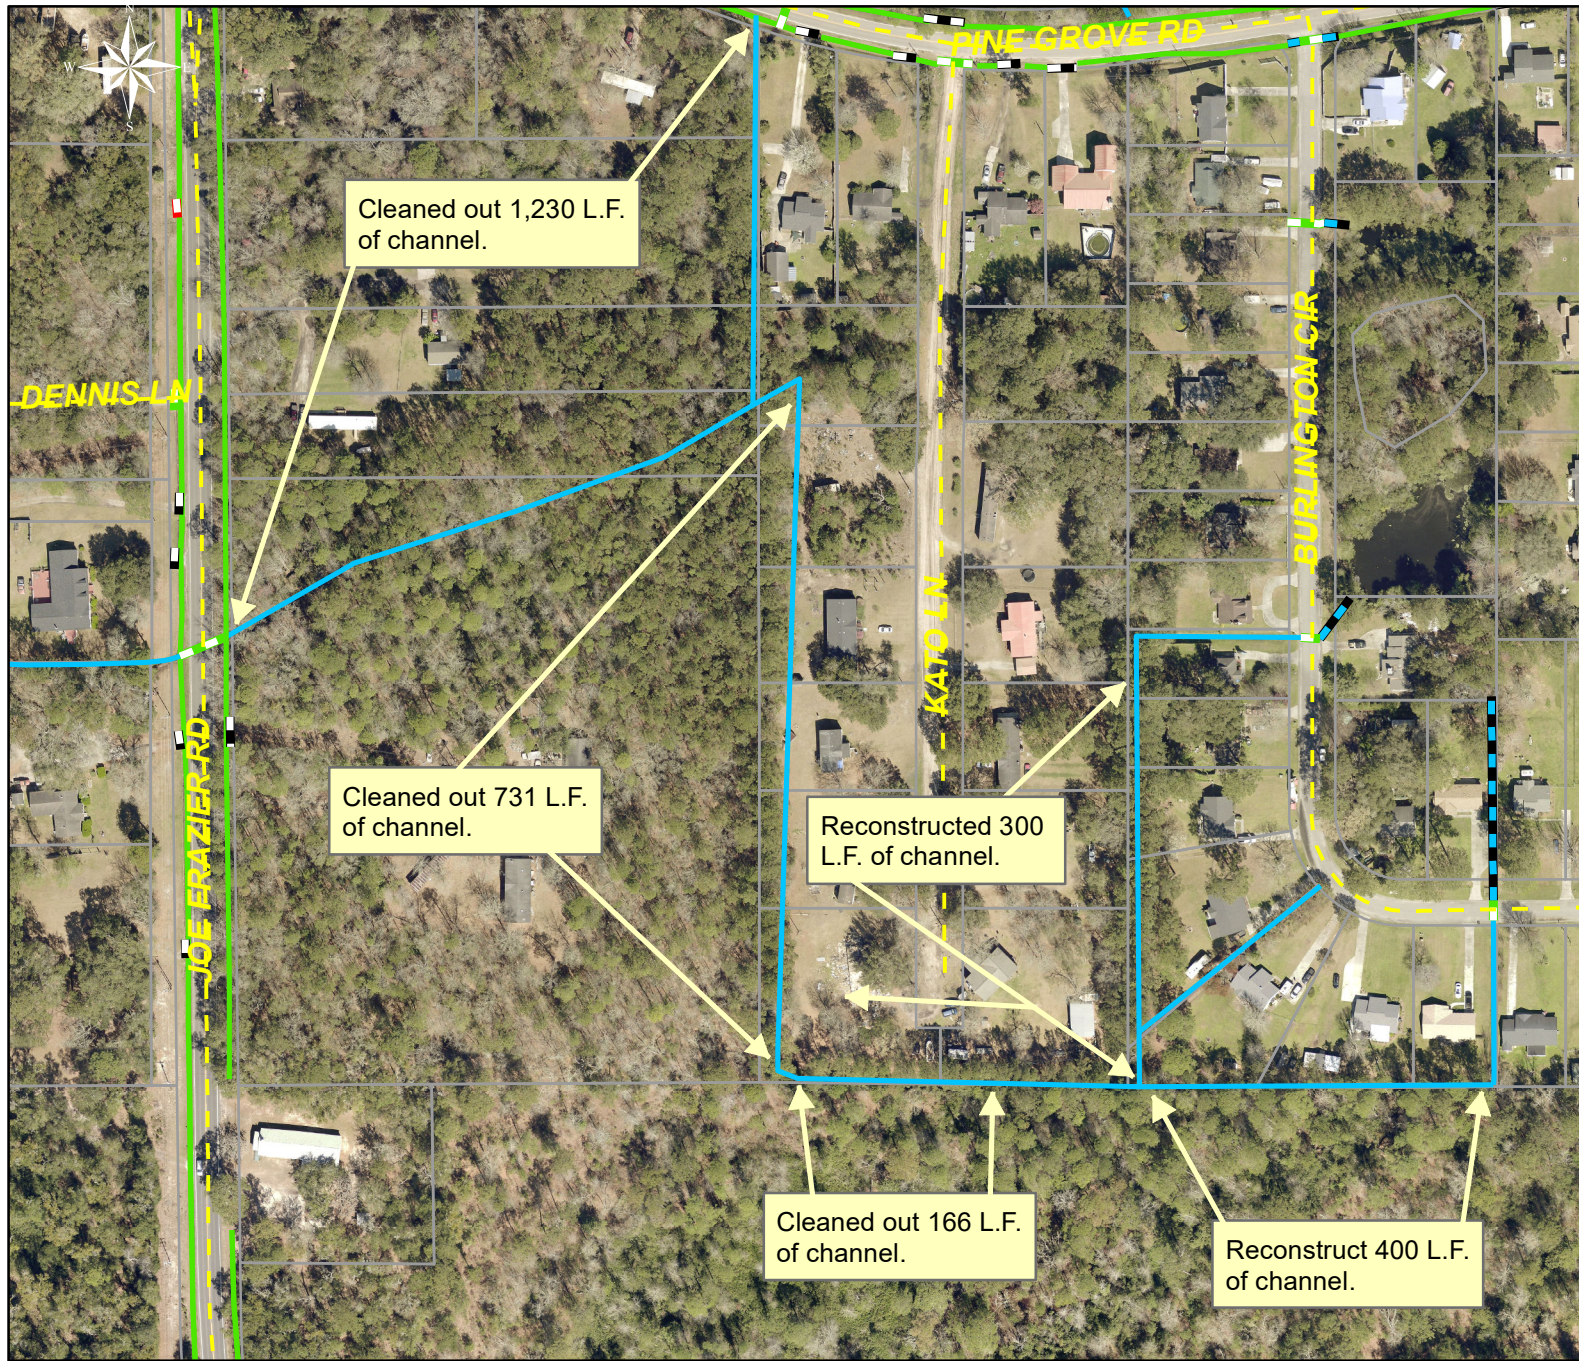

Project: Kato Lane Channel

Activity: Routine/ Preventive Maintenance

Project #: 2023-539

Township/SW Dist: Port Royal Island/6

Completed: December 2022

Legend	
Drainage Type	
	Access Pipe
	Bleeder Pipe
	Channel Pipe
	Channel
	Stream
	Crossline Pipe
	Driveway Pipe
	Lateral
	Lateral Pipe
	River
	Road Pipe
	Roadside
	Roadside Pipe



1 inch = 210 feet

Prepared By: BC Stormwater Management Utility

Date Print: 02/10/23

File: C:\esproject summaries map\Kato Lane Channel\_2023-539
