
## BEAUFORT COUNTY SALES TAX ROAD PROJECTS REVENUE/BUDGET VS EXPENDITURES As of June 30, 2014

## PRELIMINARY AND UNAUDITED


		REVENUE SOURCE/BUDGET					EXPENDITURES				ĺ
PROJECT	SALES TAX (INCLUDING CONTRIBUTIONS)	IMPACT FEES	FEDERAL/ STATE	TO	OTAL BUDGET		EXPENDITURES TO DATE	ENCUMBERED TO DATE	_	AL EXPENDED .UDING ENC.)	STATUS
US 17 WIDENING	5,052,430	2,000,000		\$	7,052,430		7,052,430	-	\$	7,052,430	COMPLETE
N BEAUFORT BYPASS	937,386			\$	937,386		937,386	-	\$	937,386	COMPLETE
US 21 BOUNDARY STREET	10,600,000	300,000	12,600,000	\$	23,500,000		12,208,586	9,563	\$	12,218,148	IN PROGRESS
BOUNDARY STREET PARALLEL ROAD	746,115			\$	746,115		746,115	-	\$	746,115	COMPLETE
SC 802 - RIBAUT ROAD	909,637			\$	909,637		906,437	-	\$	906,437	COMPLETE
US 21/SC 802 - LADY'S ISLAND DR	49,694,384			\$	49,694,384		49,138,369	14,271	\$	49,152,640	COMPLETE*
SC 802 - SAVANNAH HIGHWAY	10,106,900			\$	10,106,900		9,622,222	7,625	\$	9,629,847	COMPLETE*
BLUFFTON PARKWAY	65,916,621	1,000,000	15,000,000	\$	81,916,621		55,943,088	22,666,847	\$	78,609,935	IN PROGRESS
US 278 IMP - WILLIAM HILTON PKWY	2,963,731			\$	2,963,731		2,963,731	-	\$	2,963,731	COMPLETE
US 278 IMP - REALIGN SQUIRE POPE	1,636,140			\$	1,636,140		1,636,140	-	\$	1,636,140	COMPLETE
US 278 IMP - SIMMONSVILLE TO 170	7,701,327			\$	7,701,327		7,655,973	14,560	\$	7,670,533	COMPLETE*
US 278 IMP - FRONTAGE RDS	6,793,642			\$	6,793,642		4,938,515	121,865	\$	5,060,380	IN PROGRESS
US 278 IMP - STREET LIGHTING	164,426			\$	164,426		164,426	-	\$	164,426	COMPLETE
SC 170 WIDENING	2,000,000	1,000,000	24,900,000	\$	27,900,000		15,417,547	12,278,011	\$	27,695,559	IN PROGRESS
GRAND TOTAL	\$ 165,222,739	\$ 4,300,000	\$ 52,500,000	\$	222,022,739		\$ 169,330,966	\$ 35,112,742	\$	204,443,709	

Page 1 of 3 9/3/2014

<sup>\*</sup>Note: These projects are complete and waiting on final invoices to be provided to the County.

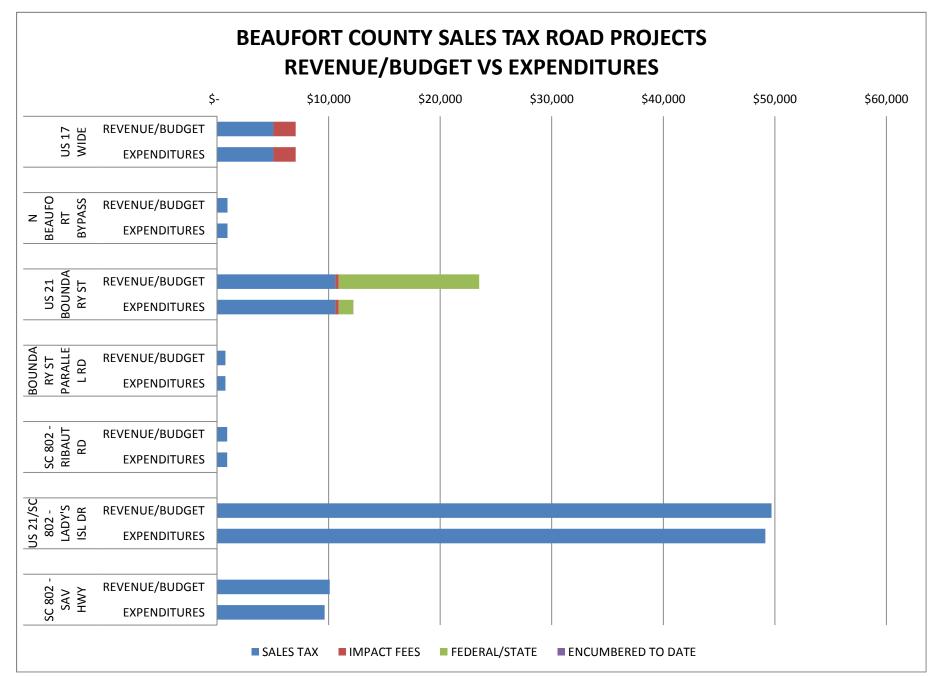

Note: Dollar amounts are in 000's.

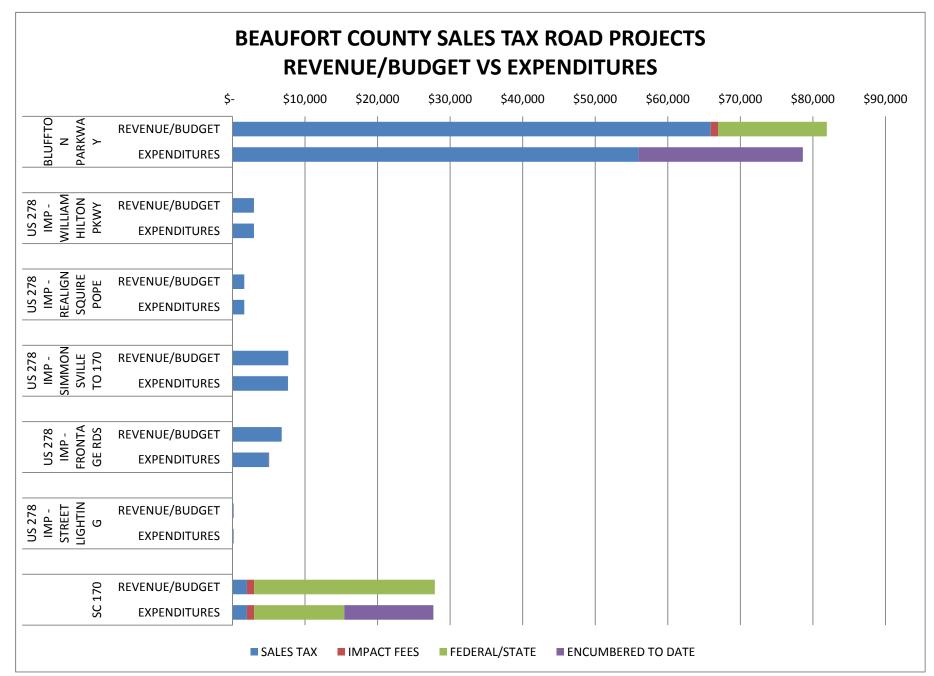

Note: Dollar amounts are in 000's.

Page 3 of 3
