Project Summary: Hilton Head Island Airport

Activity: Routine/Preventive Maintenance


Duration: 09/18/2023 - 09/26/2023

Narrative Description of Project:

Project improved 315 L.F. of drainage system. Grubbed, cleared and cleaned out 315 L.F. of channel. Installed (1) bleeder pipe and rip rap for erosion control.

2024-518 / Hilton Head Island Airport	Labor	Labor	Equipment	Material	Contractor	Total
	Hours	Cost	Cost	Cost	Cost	Cost
AUDIT / Audit Project	6.00	\$215.70	\$0.00	\$0.00	\$0.00	\$215.70
BPINST / Bleeder pipe - Installed	48.00	\$1,591.36	\$569.40	\$269.14	\$0.00	\$2,429.90
CCO / Channel - cleaned out	24.00	\$670.81	\$365.16	\$0.00	\$0.00	\$1,035.97
CGRB / Channel - grubbed	24.00	\$775.27	\$244.76	\$0.00	\$0.00	\$1,020.03
CLJS / Cleaned up jobsite	8.00	\$215.52	\$159.79	\$0.00	\$0.00	\$375.31
HAUL / Hauling	64.00	\$1,986.14	\$4,977.44	\$1,385.69	\$0.00	\$8,349.27
ONJV / Onsite Job Visit	16.00	\$546.08	\$188.00	\$0.00	\$0.00	\$734.08
RRI / Rip Rap - Installed	24.00	\$745.98	\$377.25	\$0.00	\$0.00	\$1,123.23
Grand Total	214.00	\$6,746.86	\$6,881.80	\$1,654.83	\$0.00	\$15,283.49

(No Pictures Available)

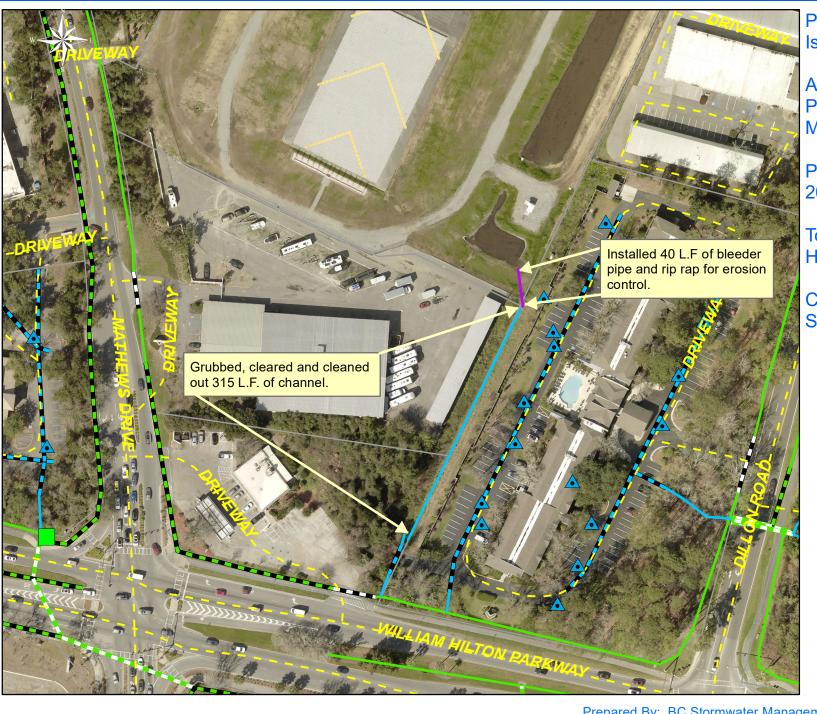

1 inch = 130 feet


Project: Hilton Head **Island Airport**

Activity: Routine/ Preventive Maintenance

Project #: 2024-518

Township/SW Dist: Hilton Head Island/3

Completed: September 2023



Prepared By: BC Stormwater Management Utility

Date Print:01/10/24

File:C:\project summaries map/HHilton Head Island Airport_2024-518
