



**Beaufort County Public Works**  
**Stormwater Infrastructure**  
*Project Summary*

**Project Summary:** Ned Court

**Activity:** Routine/Preventive Maintenance

**Duration:** 01/21/2022 - 03/03/2022

**Narrative Description of Project:**

Project improved 417 L.F. of drainage system. Cleaned out 377 L.F. of roadside ditch. Cleaned out (2) catch basins, jetted (3) driveway pipes, (1) crossline pipe and 40 L.F. of channel pipe.

**2022-539 / Ned Court**

	<b>Labor Hours</b>	<b>Labor Cost</b>	<b>Equipment Cost</b>	<b>Material Cost</b>	<b>Contractor Cost</b>	<b>Indirect Labor</b>	<b>Total Cost</b>
AUDIT / Audit Project	0.50	\$17.27	\$0.00	\$0.00	\$0.00	\$10.66	\$27.93
CBCO / Catch basin - clean out	8.00	\$261.27	\$153.28	\$77.12	\$0.00	\$164.64	\$656.31
DPJT / Driveway Pipe - Jetted	16.00	\$522.55	\$306.56	\$168.60	\$0.00	\$329.28	\$1,326.99
HAUL / Hauling	12.00	\$394.63	\$228.72	\$106.26	\$0.00	\$243.60	\$973.21
RSDCL / Roadside Ditch - Cleanout	20.00	\$648.92	\$159.55	\$163.04	\$0.00	\$237.72	\$1,209.23
UTLOC / Utility locates	0.50	\$12.35	\$0.00	\$0.00	\$0.00	\$6.62	\$18.97
<b>Grand Total</b>	<b>57.00</b>	<b>\$1,857.00</b>	<b>\$848.11</b>	<b>\$515.02</b>	<b>\$0.00</b>	<b>\$992.52</b>	<b>\$4,212.64</b>

**(Before)**



**(During)**



**(After)**







Project: Ned Court  
Map #1

Activity: Routine/  
Preventive  
Maintenance

Project #:  
2022-539

Township/SW Dist:  
Bluffton/4

Completed:  
March 2022

**Legend**

- Drainage Type**
- Access Pipe
  - Bleeder Pipe
  - Channel Pipe
  - Channel
  - Stream
  - Crossline Pipe
  - Driveway Pipe
  - Lateral
  - Lateral Pipe
  - River
  - Road Pipe
  - Roadside
  - Roadside Pipe




**1 inch = 170 feet**

Prepared By: BC Stormwater Management Utility

Date Print: 09/22/22

File: C:\project summaries map\Ned Court Map#1\_2022-539



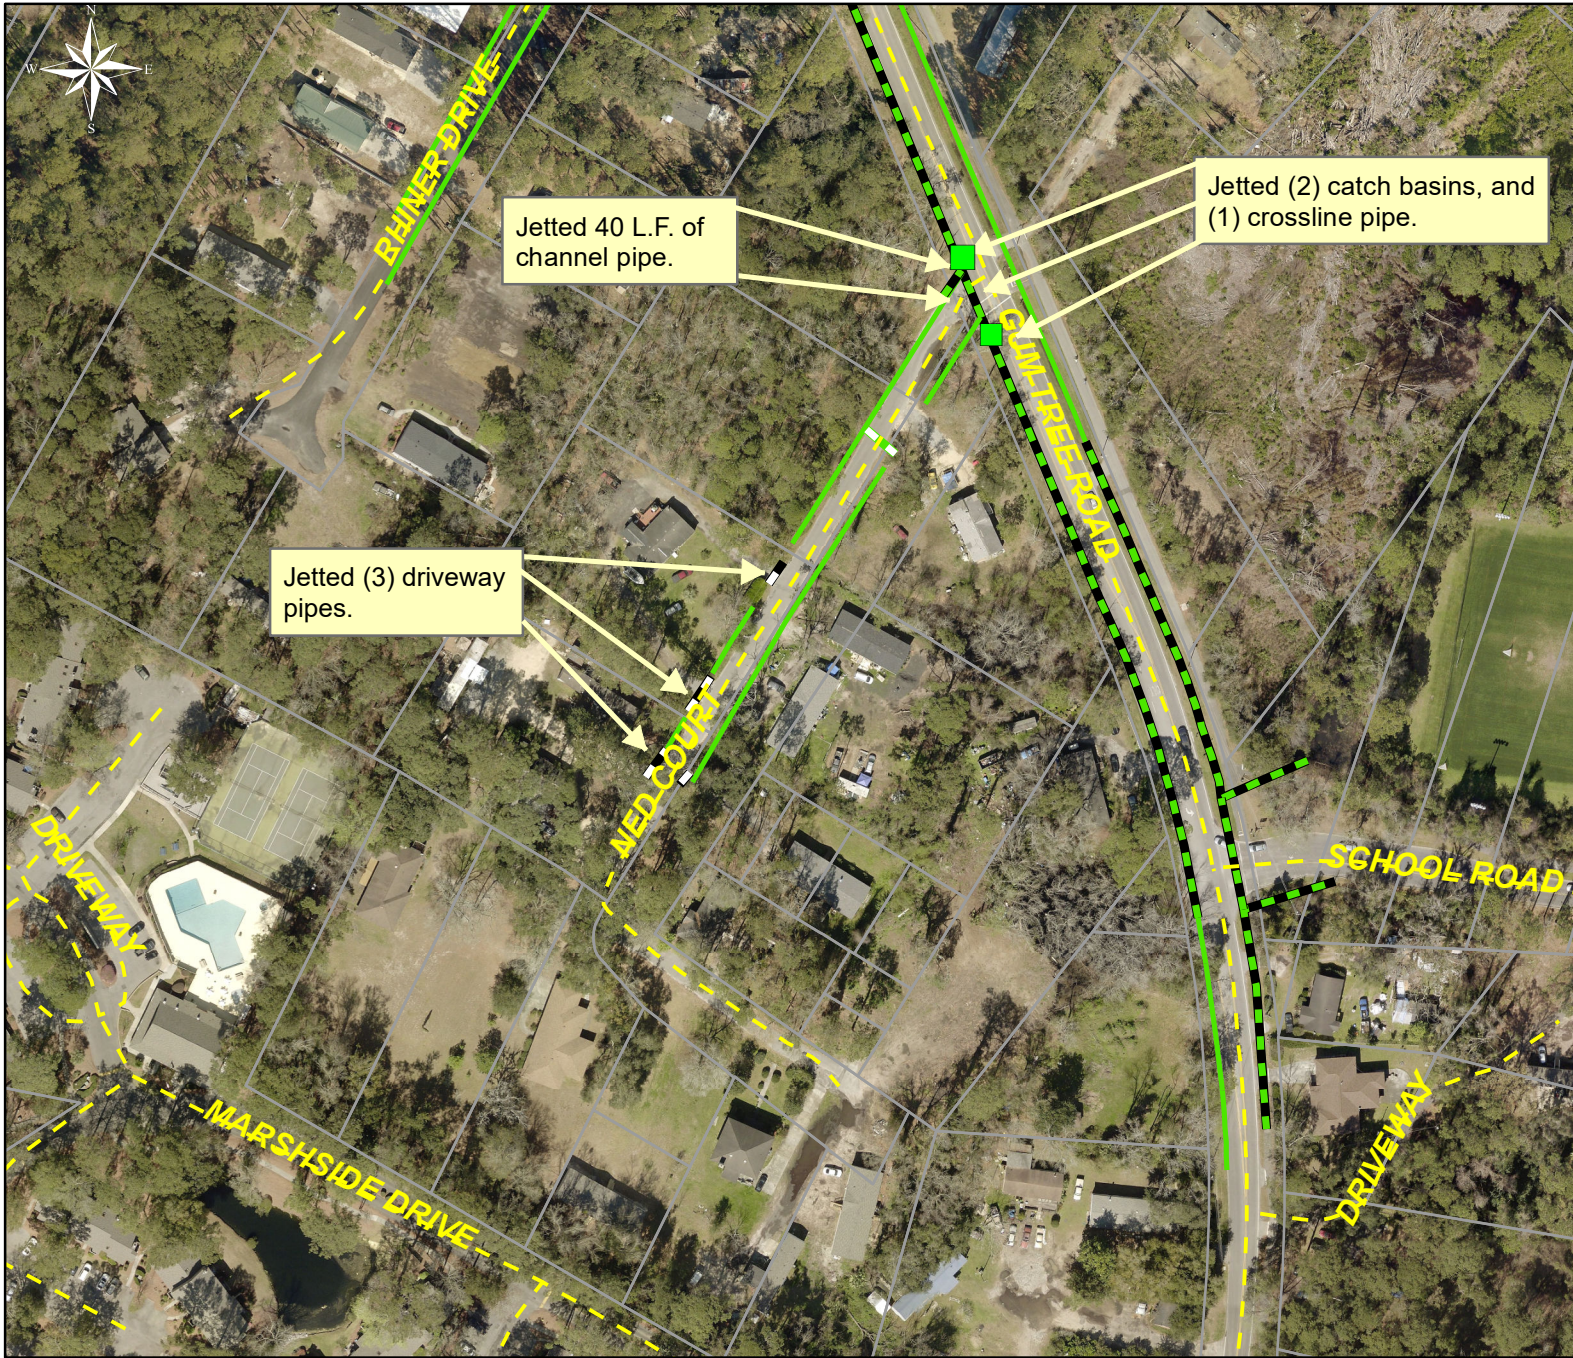

Project: Ned Court  
Map #2

Activity: Routine/  
Preventive  
Maintenance














Project #:  
2022-539

Township/SW Dist:  
Bluffton/4

Completed:  
March 2022

**Legend**

**Drainage Type**

-  Access Pipe
-  Bleeder Pipe
-  Channel Pipe
-  Channel
-  Stream
-  Crossline Pipe
-  Driveway Pipe
-  Lateral
-  Lateral Pipe
-  River
-  Road Pipe
-  Roadside
-  Roadside Pipe



**1 inch = 170 feet**

Prepared By: BC Stormwater Management Utility

Date Print: 09/22/22

File: C:\project summaries map\Ned Court Map#2 \_2022-539
