

## Beaufort County Public Works Stormwater Infrastructure

**Project Summary** 

Project Summary: Ned Court Activity: Routine/Preventive Maintenance

**Duration:** 01/21/2022 - 03/03/2022

## **Narrative Description of Project:**

Project improved 417 L.F. of drainage system. Cleaned out 377 L.F. of roadside ditch. Cleaned out (2) catch basins, jetted (3) driveway pipes, (1) crossline pipe and 40 L.F. of channel pipe.


2022-539 / Ned Court	Labor	Labor	Equipment	Material	Contractor	Indirect	Total
	Hours	Cost	Cost	Cost	Cost	Labor	Cost
AUDIT / Audit Project	0.50	\$17.27	\$0.00	\$0.00	\$0.00	\$10.66	\$27.93
CBCO / Catch basin - clean out	8.00	\$261.27	1 \$153.28	\$77.12	\$0.00	\$164.64	\$656.31
DPJT / Driveway Pipe - Jetted	16.00	\$522.55	\$306.56	\$168.60	\$0.00	\$329.28	\$1,326.99
HAUL / Hauling	12.00	\$394.63	\$228.72	\$106.26	\$0.00	\$243.60	\$973.21
RSDCL / Roadside Ditch - Cleanout	20.00	\$648.92	\$159.55	\$163.04	\$0.00	\$237.72	\$1,209.23
UTLOC / Utility locates	0.50	\$12.35	\$0.00	\$0.00	\$0.00	\$6.62	\$18.97
Grand Total	57.00	\$1,857.00	\$848.11	\$515.02	\$0.00	\$992.52	\$4,212.64

(Before) (During) (After)







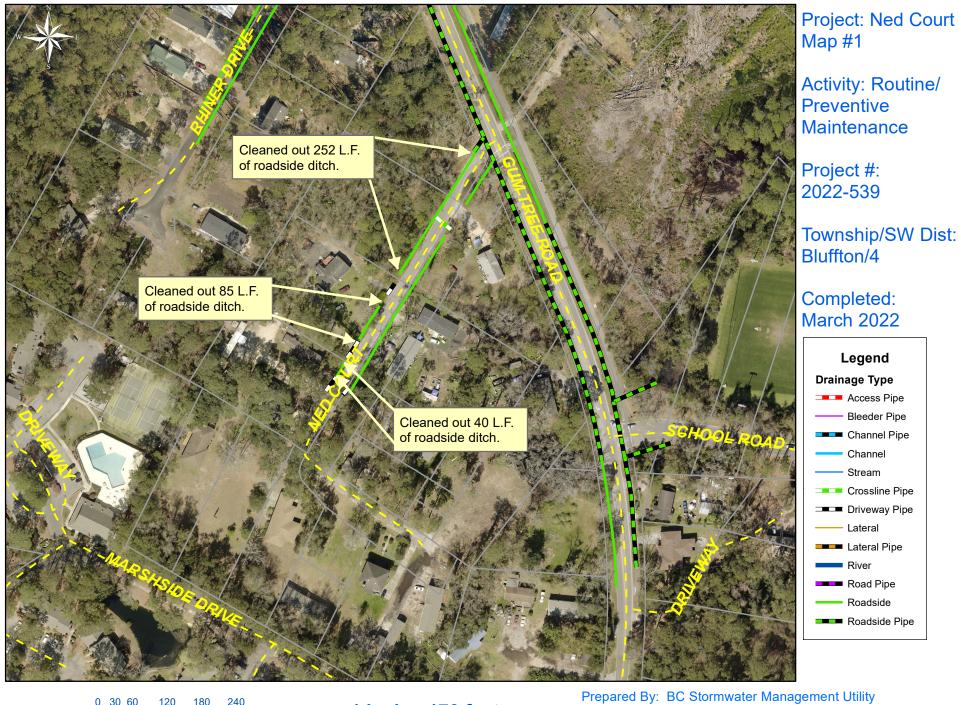


180 240 Feet 0 30 60 120

1 inch = 170 feet

Date Print:09/22/22

File:C:\project summaries map/Ned Court Map#1\_2022-539

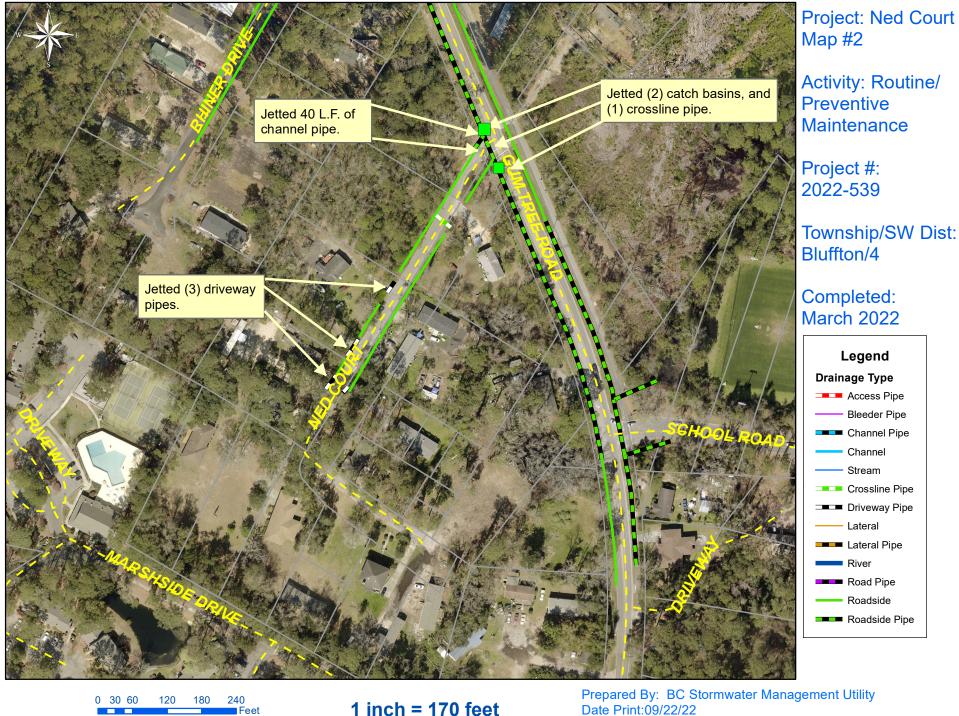

1 inch = 170 feet

Date Print:09/22/22

File:C:\project summaries map/Ned Court Map#2 \_2022-539
