



Beaufort County
Public Works
Stormwater Infrastructure
Project Summary

Project Summary: Tanglewood Drive

Activity: Routine/Preventive Maintenance

Narrative Description of Project:

Duration: 3/15/16 - 4/28/16

Project improved 2,622 L.F. of drainage system. Cleaned out 1,779 L.F. of roadside ditch. Jetted (3) crossline pipes, (7) driveway pipes and 843 L.F. of roadside pipe. Repaired washout. Hydroseeded for erosion control.

2016-589 / Tanglewood Drive	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Labor	Total Cost
AUDIT / Audit Project	0.5	\$11.75	\$0.00	\$0.00	\$0.00	\$6.62	\$18.36
CLPJT / Crossline Pipe - Jetted	33.0	\$755.04	\$143.22	\$55.69	\$0.00	\$490.05	\$1,444.00
DPJT / Driveway Pipe - Jetted	8.0	\$183.04	\$34.72	\$24.11	\$0.00	\$118.80	\$360.67
HAUL / Hauling	45.0	\$1,002.15	\$359.55	\$124.60	\$0.00	\$648.90	\$2,135.20
ONJV / Onsite Job Visit	15.0	\$512.70	\$53.10	\$39.76	\$0.00	\$367.05	\$972.61
RDREC / Roadside ditch - reconstructed	9.0	\$209.24	\$53.47	\$82.46	\$0.00	\$129.42	\$474.59
RPWO / Repaired Washout	10.0	\$225.20	\$48.11	\$7.55	\$0.00	\$133.35	\$414.21
RSDCL / Roadside Ditch - Cleanout	214.0	\$4,530.24	\$1,206.76	\$180.56	\$0.00	\$2,859.22	\$8,776.78
UTLOC / Utility locates	0.5	\$12.35	\$0.00	\$0.00	\$0.00	\$6.62	\$18.97
2016-589 / Tanglewood Drive Sub Total	335.0	\$7,441.70	\$1,898.93	\$514.73	\$0.00	\$4,760.02	\$14,615.38
 Grand Total	335.0	\$7,441.70	\$1,898.93	\$514.73	\$0.00	\$4,760.02	\$14,615.38

Before



During



After





Project: Tanglewood Drive
Map 1

Activity: Routine/
Preventive
Maintenance

Project #:
2016-589

Township/SW Dist:
Port Royal Island/
2&6


Completed:
April 2016

Legend	
Drainage Type	
	Access Pipe
	Bleeder Pipe
	Channel Pipe
	Channel
	Stream
	Crossline Pipe
	Driveway Pipe
	Lateral
	Lateral Pipe
	River
	Road Pipe
	Roadside
	Roadside Pipe

0 40 80 160 240 320
Feet

1 inch = 170 feet

Prepared By: BC Stormwater Management Utility
Date Print: 07/18/16
File: C:\project summaries map\Tanglewood Drive Map 1_2016-589

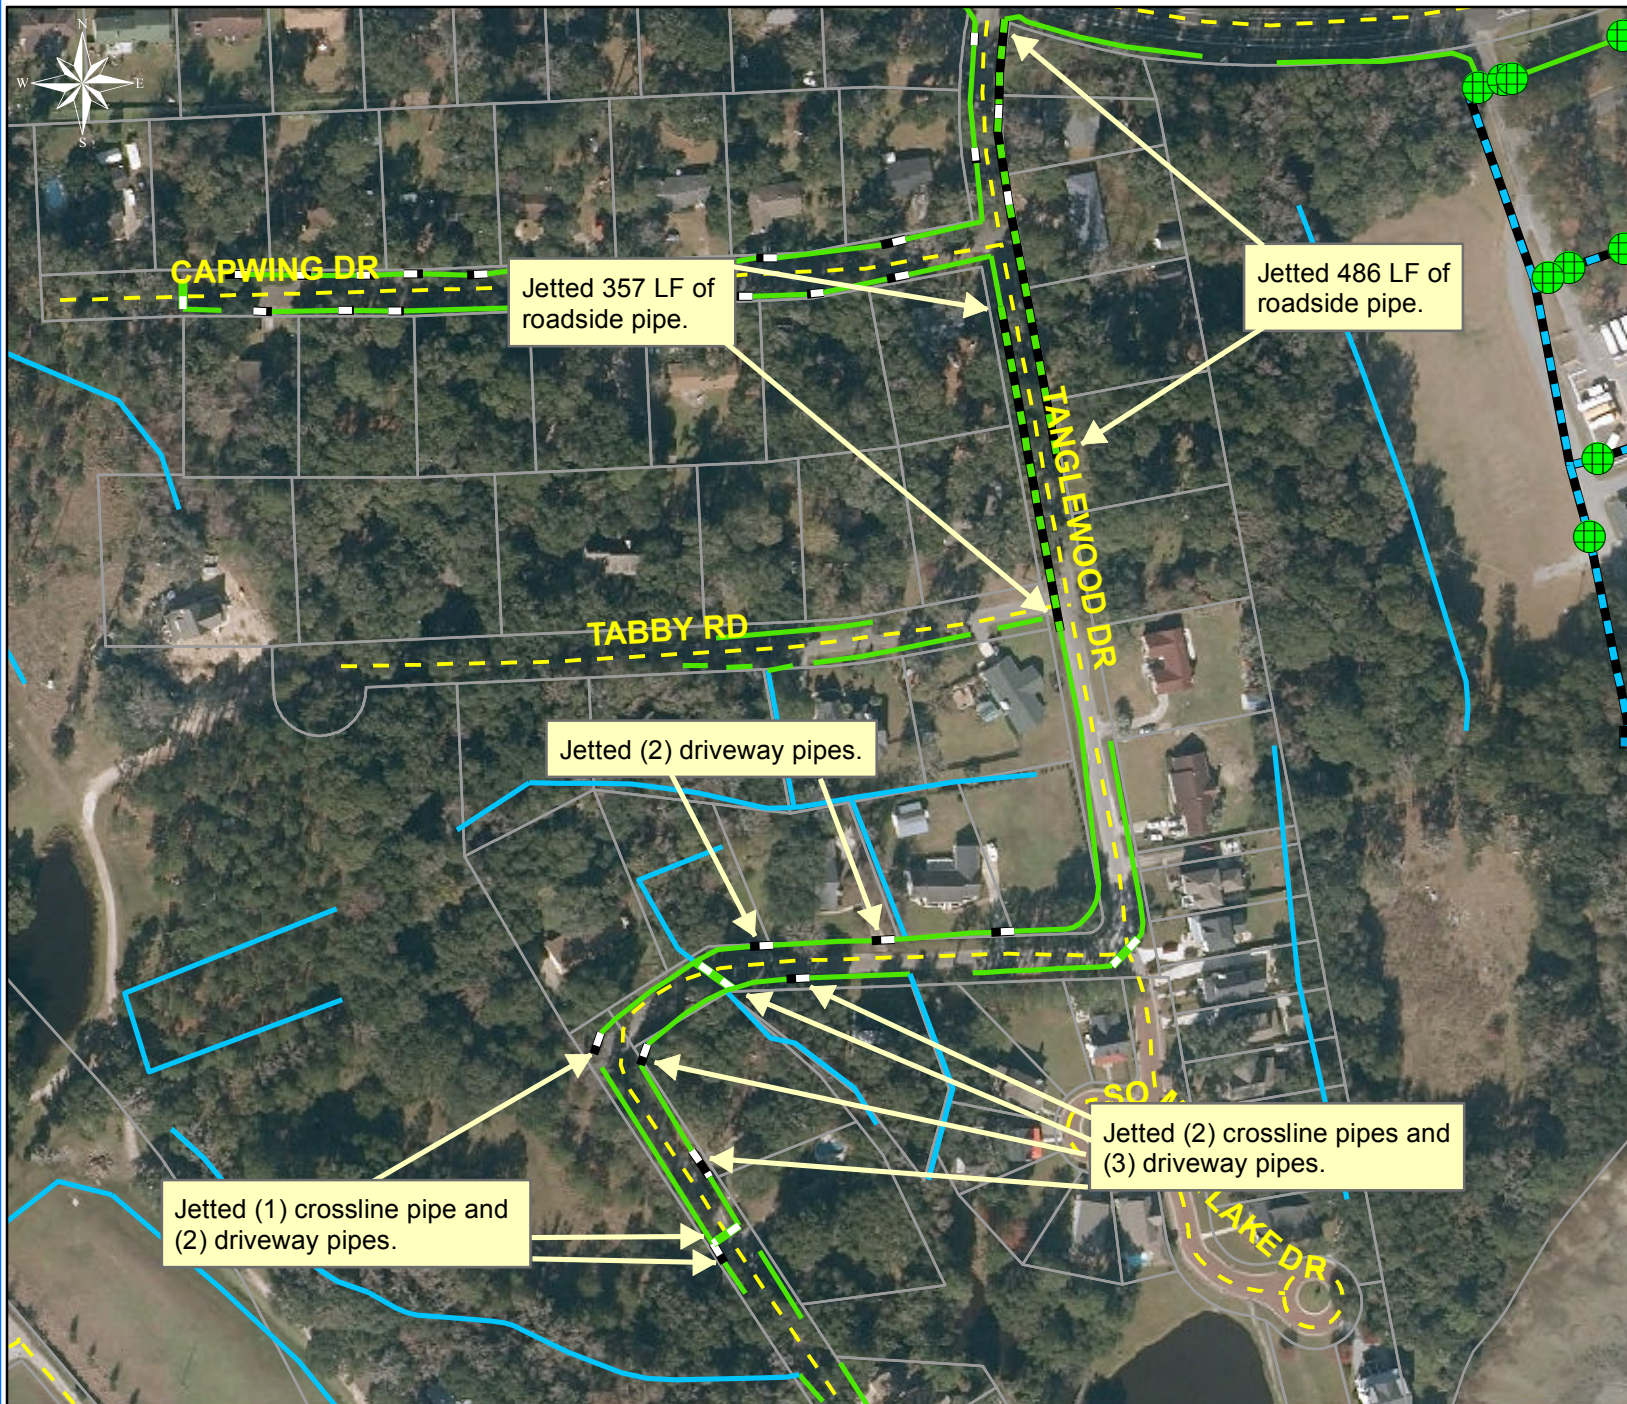

Project: Tanglewood Drive
Map 2

Activity: Vacuum Truck

Project #: 2016-589

Township/SW Dist: Port Royal Island/ 2&6

Completed: April 2016

Legend

Drainage Type

- Access Pipe
- Bleeder Pipe
- Channel Pipe
- Channel
- Stream
- Crossline Pipe
- Driveway Pipe
- Lateral
- Lateral Pipe
- River
- Road Pipe
- Roadside
- Roadside Pipe

0 50 100 200 300 400 Feet

1 inch = 210 feet
