



Beaufort County Public Works
Stormwater Infrastructure
Project Summary

Project Summary: Camp St Marys Road and Okatie Bluff Road

Activity: Routine/Preventive Maintenance

Duration: 11/21/2022 - 11/22/2022

Narrative Description of Project:

Project improved 100 L.F. of drainage system. Cleaned out 100 L.F. of roadside ditch, repaired (1) crossline pipe and (1) sinkhole.

2023-540 / Camp St Marys Road and Okatie Bluff Road	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Cost	Total Cost
AUDIT / Audit Project	0.50	\$16.37	\$0.00	\$0.00	\$0.00	\$10.11	\$26.48
CPREP / Crossline Pipe - Repaired	40.00	\$978.51	\$185.28	\$168.86	\$0.00	\$389.52	\$1,722.17
HAUL / Hauling	16.00	\$479.52	\$304.96	\$1,429.09	\$0.00	\$0.00	\$2,213.57
ONJV / Onsite Job Visit	16.00	\$667.52	\$69.60	\$17.40	\$0.00	\$0.00	\$754.52
RSDCL / Roadside Ditch - Cleanout	40.00	\$978.51	\$235.44	\$94.60	\$0.00	\$389.52	\$1,698.07
Grand Total	112.50	\$3,120.43	\$795.28	\$1,709.95	\$0.00	\$789.15	\$6,414.80

Before




During



After



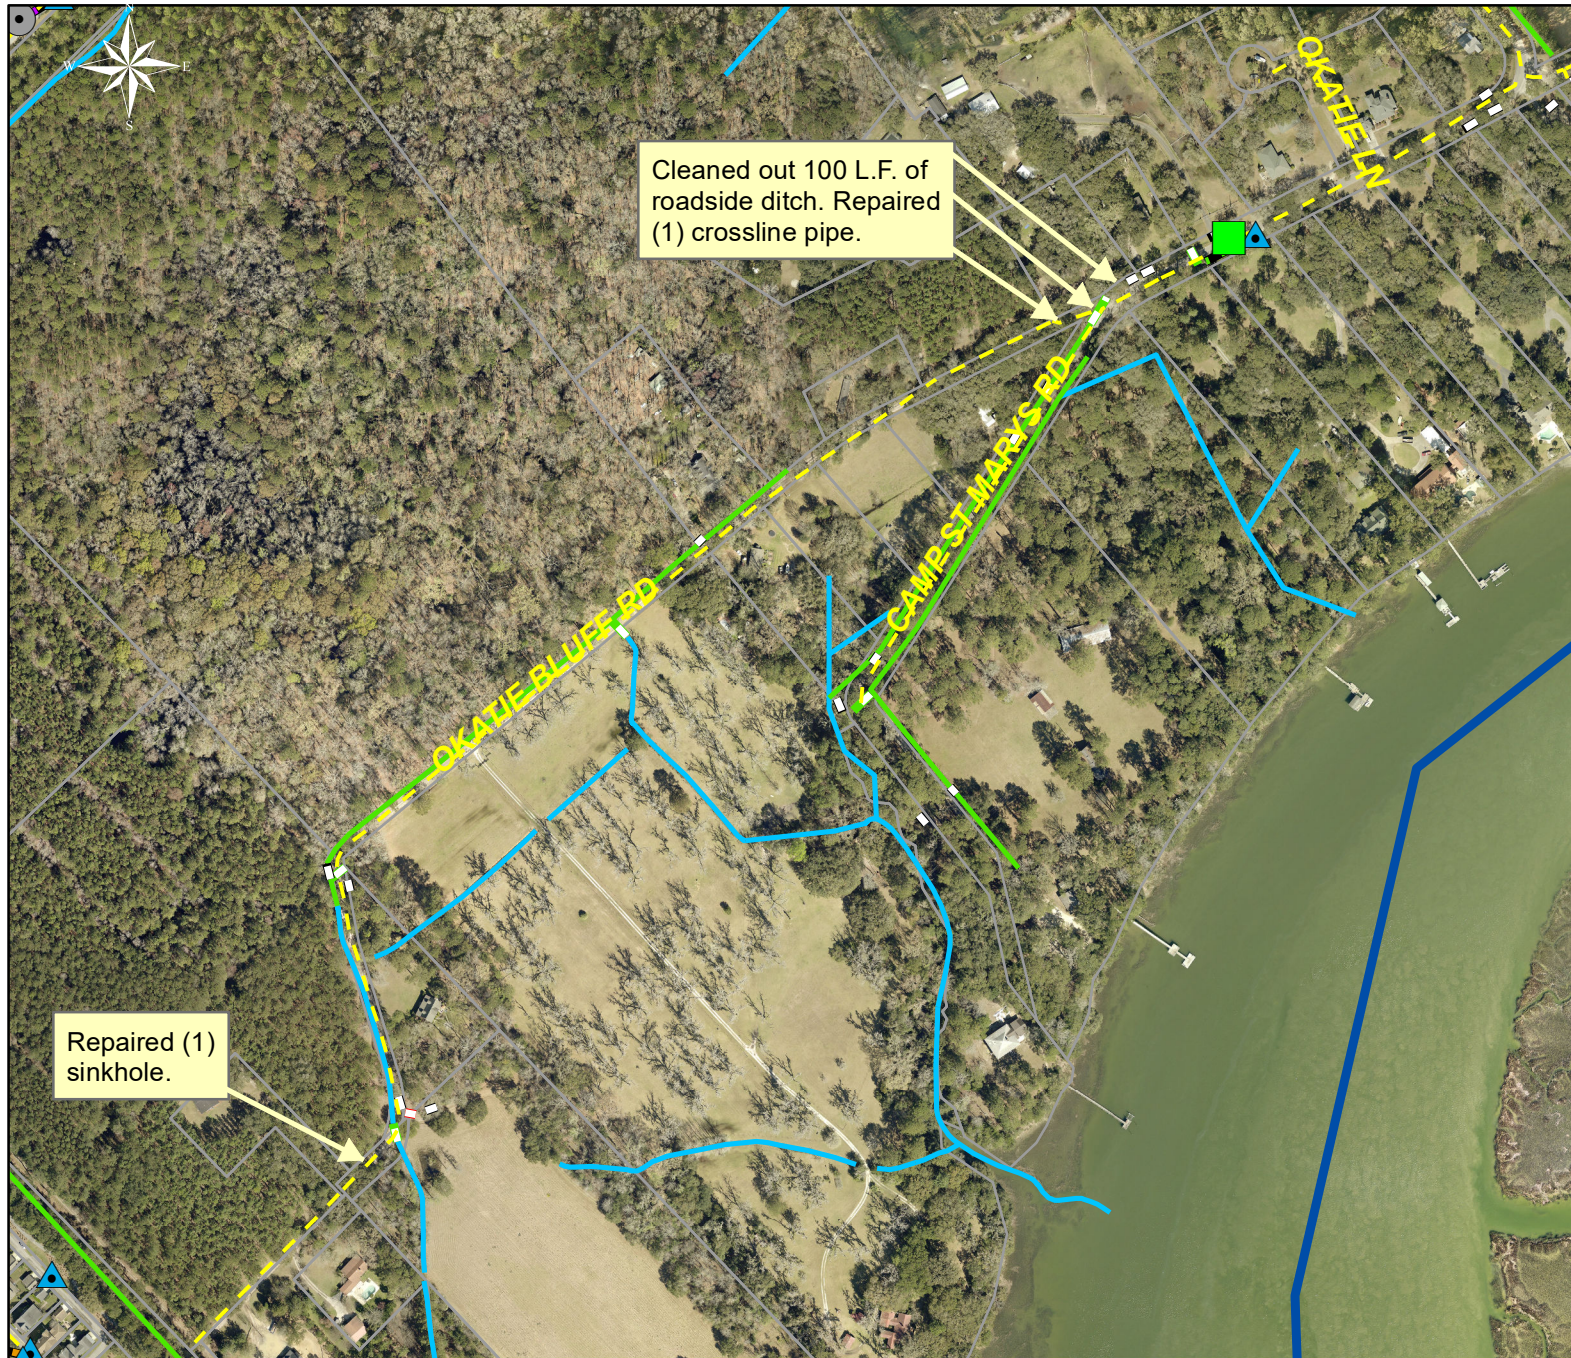

Project: Camp St. Marys Road and Okatie Bluff Road

Activity: Routine/ Preventive Maintenance














Project #: 2023-540

Township/SW Dist: Bluffton/4

Completed: November 2022

Legend

Drainage Type

-  Access Pipe
-  Bleeder Pipe
-  Channel Pipe
-  Channel
-  Stream
-  Crossline Pipe
-  Driveway Pipe
-  Lateral
-  Lateral Pipe
-  River
-  Road Pipe
-  Roadside
-  Roadside Pipe

0 80 160 320 480 640 Feet

1 inch = 420 feet

Prepared By: BC Stormwater Management Utility

Date Print: 03/20/23

File: C:\esproject summaries map\Camp St. Marys and Okatie Bluff Road_2023-540
