



**Beaufort County Public Works**  
**Stormwater Infrastructure**  
Project Summary

**Project Summary:** Passive Parks - Eugene Drive (Reimbursement)

**Activity:** Routine/Preventive Maintenance

**Duration:** 06/07/2023

**Narrative Description of Project:**

This project improved 40 L.F of drainage system. Cleaned out 40 L.F. of channel, removed (2) access pipes, constructed berms, and handseeded for erosion control.

<b>2023-611 / Passive Parks - Eugene Drive (Reimbursement)</b>	<b>Labor Hours</b>	<b>Labor Cost</b>	<b>Equipment Cost</b>	<b>Material Cost</b>	<b>Contractor Cost</b>	<b>Indirect Cost</b>	<b>Total Cost</b>
APREM / Access pipe - removed	8.00	\$208.56	\$34.80	\$87.00	\$0.00	\$128.72	\$459.08
AUDIT / Audit Project	1.00	\$33.73	\$0.00	\$0.00	\$0.00	\$20.82	\$54.55
BERM / Berm Construction	16.00	\$563.11	\$135.12	\$244.18	\$0.00	\$347.60	\$1,290.01
HAUL / Hauling	8.00	\$268.36	\$304.96	\$64.02	\$0.00	\$165.64	\$802.98
ONJV / Onsite Job Visit	11.00	\$532.54	\$47.85	\$20.30	\$0.00	\$331.14	\$931.83
PA / Project Assit	4.00	\$126.04	\$0.00	\$0.00	\$0.00	\$77.80	\$203.84
STBY / Stand By	4.00	\$142.32	\$0.00	\$0.00	\$0.00	\$87.84	\$230.16
<b>Grand Total</b>	<b>52.00</b>	<b>\$1,874.66</b>	<b>\$522.73</b>	<b>\$415.50</b>	<b>\$0.00</b>	<b>\$1,159.56</b>	<b>\$3,972.46</b>

**Before**




**During**



**After**



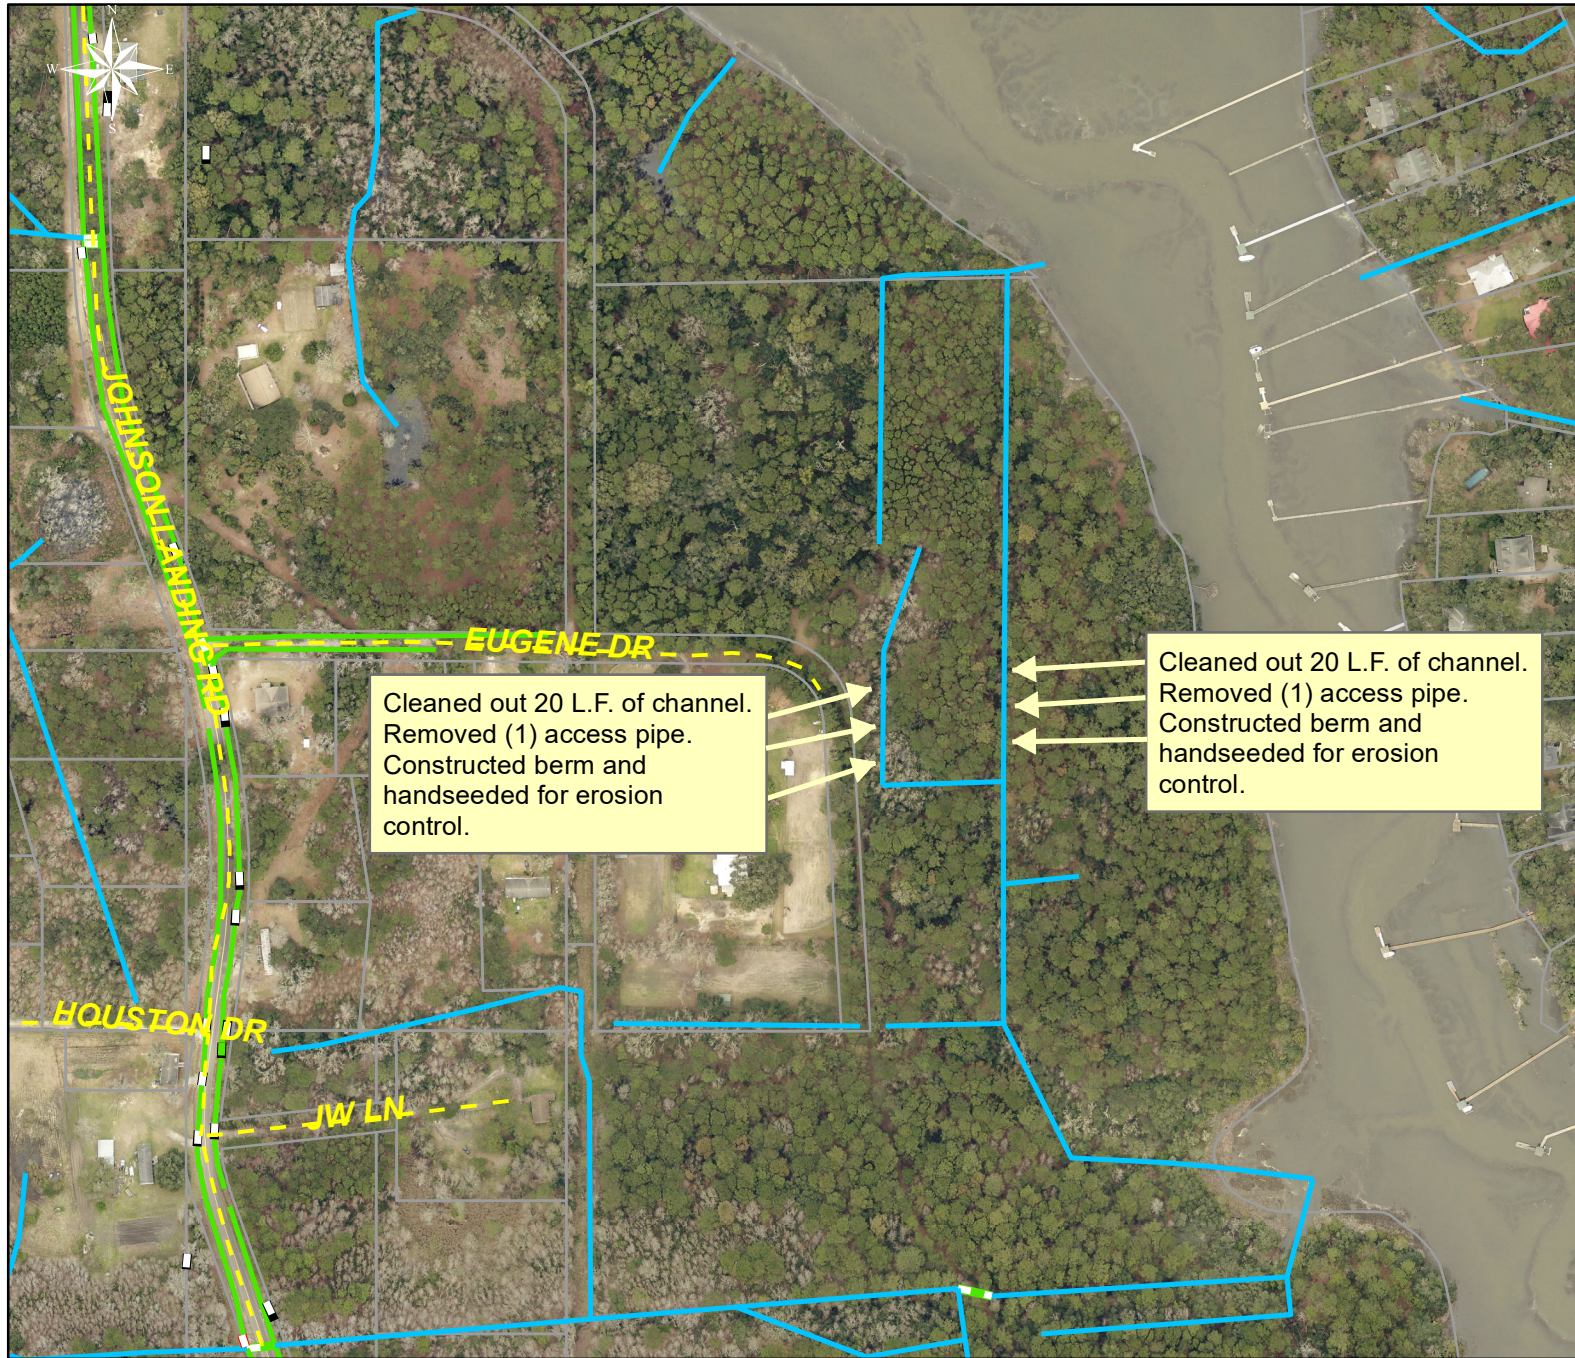

Project: Passive  
Parks - Eugene  
Drive  
(Reimbursement)

Activity: Routine/  
Preventive  
Maintenance














Project #:  
2023-611

Township/SW Dist:  
Lady's Island/7

Completed:  
June 2023

**Legend**

**Drainage Type**

-  Access Pipe
-  Bleeder Pipe
-  Channel Pipe
-  Channel
-  Stream
-  Crossline Pipe
-  Driveway Pipe
-  Lateral
-  Lateral Pipe
-  River
-  Road Pipe
-  Roadside
-  Roadside Pipe

Cleaned out 20 L.F. of channel.  
Removed (1) access pipe.  
Constructed berm and  
handseeded for erosion  
control.

Cleaned out 20 L.F. of channel.  
Removed (1) access pipe.  
Constructed berm and  
handseeded for erosion  
control.

0 70 140 280 420 560  
Feet

**1 inch = 330 feet**

Prepared By: BC Stormwater Management Utility

Date Print:06/12/23

File:C:\project summaries map\Passive Park- Eugene Drive Reimbursement\_2023-611
