



Beaufort County Public Works
Stormwater Infrastructure
Project Summary

Project Summary: Eustis Landing Road

Activity: Routine/Preventive Maintenance

Duration: 03/14/2023 - 04/25/2023

Narrative Description of Project:

Project improved 1,378 L.F. of drainage system. Cleaned out 1,378 L.F. of roadside ditch. Jetted (8) driveway pipes and hydroseeded for erosion control.

2023-591 / Eustis Landing Road

	Labor Hours	Labor Cost	Equipment Cost	Material Cost	Contractor Cost	Indirect Cost	Total Cost
AUDIT / Audit Project	2.00	\$65.48	\$0.00	\$0.00	\$0.00	\$40.42	\$105.90
DPJT / Driveway Pipe - Jetted	8.00	\$251.68	\$153.28	\$46.14	\$0.00	\$155.36	\$606.46
HAUL / Hauling	24.00	\$719.28	\$457.44	\$1,098.78	\$0.00	\$0.00	\$2,275.50
HYDR / Hydroseeding	24.00	\$681.28	\$116.44	\$398.77	\$0.00	\$107.28	\$1,303.77
PRRECON / Project Reconnaissance	12.00	\$340.64	\$17.40	\$10.76	\$0.00	\$53.64	\$422.44
RSDCL / Roadside Ditch - Cleanout	36.00	\$1,021.92	\$284.30	\$121.92	\$0.00	\$160.92	\$1,589.06
Grand Total	106.00	\$3,080.28	\$1,028.86	\$1,676.37	\$0.00	\$517.62	\$6,303.13

Before



During



After




Project: Eustis Landing Road

Activity: Routine/
Preventive
Maintenance

Project #:
2023-591

Township/SW Dist:
Lady's Island/7

Completed:
April 2023

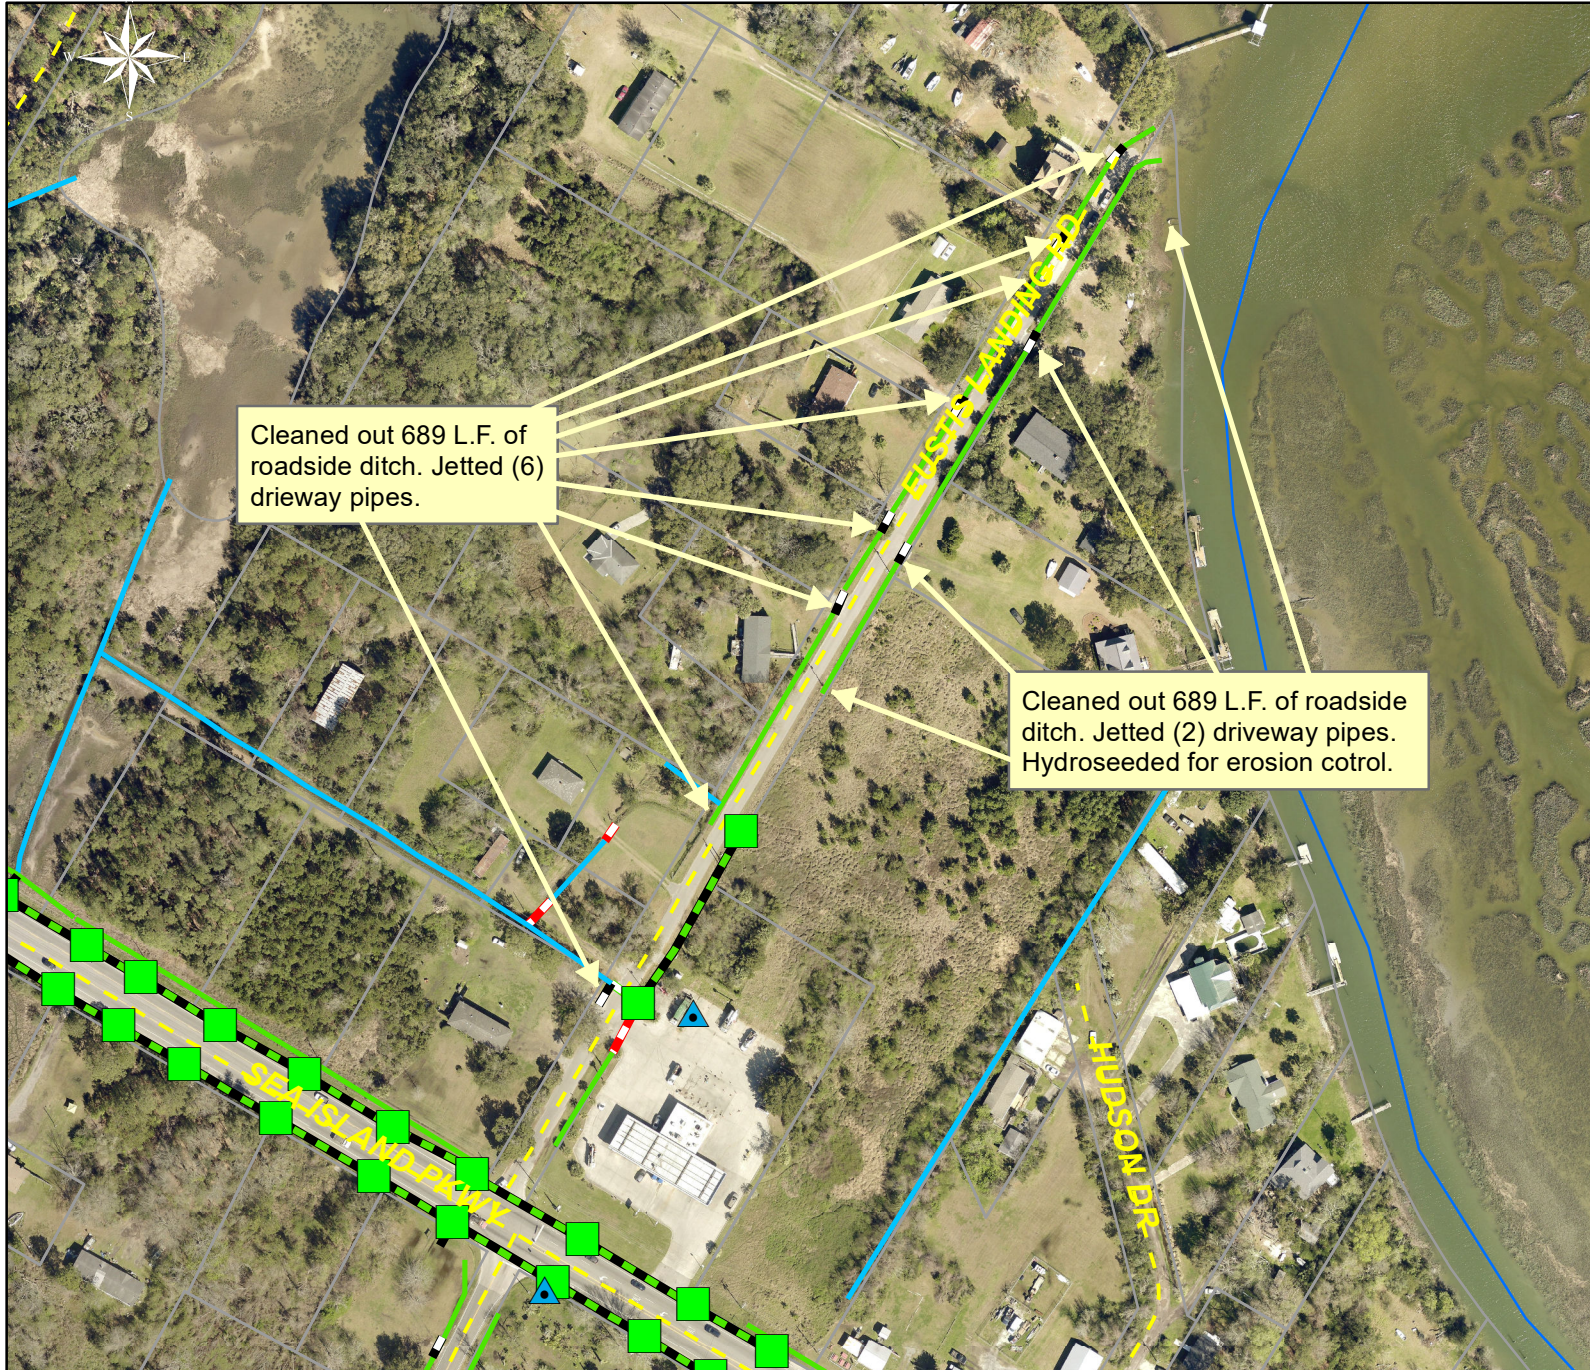

Legend	
Drainage Type	
	Access Pipe
	Bleeder Pipe
	Channel Pipe
	Channel
	Stream
	Crossline Pipe
	Driveway Pipe
	Lateral
	Lateral Pipe
	River
	Road Pipe
	Roadside
	Roadside Pipe

0 45 90 180 270 360
Feet

1 inch = 210 feet

Prepared By: BC Stormwater Management Utility
Date Print:05/01/23
File:C:\esproject summaries map\Eustis Landing Road_2023-591
